




Primavera P6 EPPM Reports Tab Samples

The following are some samples of the standard reports available in the Oracle Primavera P6 EPPM Reports Tab. This tab is available when P6 is integrated with Oracle Business Intelligence (BI) Publisher.



Ten Six Consulting offer BI Publisher integration services, BI Publisher training and BI Publisher report development services. Follow these links for more information.

Integration Services:

<http://www.tensixconsulting.com/software-services/primavera-implementation-consulting/primavera-integration/>

BI Publisher Training:

<http://www.tensixconsulting.com/oracle-business-intelligence-publisher/>

BI Publisher Services:

<http://www.tensixconsulting.com/primavera-p6-bi-publisher-services/>

<http://www.tensixconsulting.com>

Primavera P6 EPPM Reports Tab BI Publisher Samples

Sample Primavera P6 EPPM (BI Publisher) Reports included in this document are:

Cross Project Relationships - 3

Activity Look Ahead – 4

Duration Analysis – 5

Activity Relationships – 6

Activity Resource Assignments – 7

Schedule Report with Notebooks – 8

Resource Role Skill Sets – 9

Resource Code Assignments – 10

Resource Role Associations – 11

Code Assignments – 12

Project Portfolio Review – 13

Portfolio Counts – 16

Document Assignments – 17

Risk Scoring Report – 18

Project Status Report – 19

Qualitative Risk Report – 20

Project Hierarchy Including Steps – 21

Users – 22

Project Template Management – 23

Portfolio Privileges – 24

Calendar User – 27

Cross Project Relationships

Project Name / Activity Name (Critical, Relationship Type, Driving, Lag)

Predecessor Projects impacting City Center Office Building Addition

Haitang Corporate Park / Begin Building Construction (No, Start to Start, No, 0)
Haitang Corporate Park / Review and Approve Flooring (No, Finish to Start, No, 0)
Haitang Corporate Park / Foundation Phase Complete (No, Finish to Start, No, 0)
Haitang Corporate Park / Connect Equipment (No, Finish to Start, Yes, 0)
Haitang Corporate Park / Structure Complete (No, Finish to Start, Yes, 0)
Haitang Corporate Park / Finish Carpentry and Millwork (Yes, Finish to Start, Yes, 0)

Successor Projects impacted by City Center Office Building Addition

Nesbid Building Expansion / Rough-In Phase Begins (No, Finish to Start, Yes, 0)
Nesbid Building Expansion / Drywall in Offices (Yes, Finish to Start, Yes, 0)
Nesbid Building Expansion / Award Contract for Flooring (No, Finish to Start, Yes, 0)
Nesbid Building Expansion / Begin Building Construction (No, Finish to Start, Yes, 0)
Nesbid Building Expansion / Erect Structural Frame (No, Finish to Start, Yes, 0)
Nesbid Building Expansion / Floor Decking (No, Finish to Start, Yes, 0)

Activity Look Ahead

Activity Name(ID)	Status	Critical	Percent Complete	Start	Finish
Prepare and Solicit Bids for Flooring(EC1170)	In Progress	N	95	04/04/2011	05/06/2011
Prepare and Solicit Bids for Heat Pump(EC1190)	In Progress	Y	92	04/14/2011	05/03/2011
Excavation(EC1230)	Not Started	N	0	05/02/2011	06/02/2011
Review Bids for Heat Pump(EC1240)	Not Started	Y	0	05/03/2011	05/17/2011
Review Bids for Flooring(EC1250)	Not Started	N	0	05/06/2011	05/27/2011
Award Contract for Brick(EC1260)	In Progress	N	8	04/21/2011	05/05/2011
Deliver Brick(EC1280)	Not Started	N	0	05/05/2011	05/06/2011

Duration Analysis

Activity	Planned Duration	Actual Duration	High Estimate (25%)	Low Estimate (20%)	Variance %
Set Heat Pump	96	0	120	77	0
Rough-In Plumbing/Piping	19	0	24	15	0
Touch-up and Clean-up	19	0	24	15	0
Fabricate and Deliver Heat Pump and Controls	3283	0	4104	2627	0
Install Underground Water Lines	96	0	120	77	0
Form/Pour Concrete Footings	184	0	230	147	0
Concrete Foundation Walls	192	0	240	154	0
Erect Structural Frame	378	0	472	302	0
Floor Decking	251	0	314	201	0
Concrete First Floor	288	0	360	230	0
Install AC Grills and Registers	40	0	50	32	0
Assemble Brick Samples	0	0	0	0	0
Assemble and Submit Flooring Samples	0	0	0	0	0
Start Office Building Addition Project	0	0	0	0	0
Award Contract for Heat Pump	48	0	60	38	0
Assemble Technical Data for Heat Pump	58	58	72	46	100
Form and Pour Slab	88	0	110	70	0
Begin Structural Phase	0	0	0	0	0
Concrete Second Floor	288	0	360	230	0
Install Door and Window Frames	19	0	24	15	0
Install Exterior Doors and Windows	38	0	48	31	0
Prepare and Solicit Bids for Heat Pump	115	92	144	92	80
Finish Carpentry and Millwork	96	0	120	77	0
Building Addition Complete	0	0	0	0	0
Install Lighting Fixtures	58	0	72	46	0
Prepare and Solicit Bids for Brick Exterior	115	139	144	92	121

Activity Relationships

Activity Name	Responsibility	Activity Status	Start	Finish
Design Building Addition	MILLS	Completed	05/01/2011	05/01/2011
	Pred Name		Responsibility	Finish
	Start Office Building Addition Project		FOLEY	05/01/2011
	Succ. Name		Responsibility	Start
	Review and Approve Designs		MILLS	05/01/2011
Start Office Building Addition Project	FOLEY	Completed	05/01/2011	05/01/2011
	Succ. Name		Responsibility	Start
	Design Building Addition		MILLS	05/01/2011
Review and Approve Designs	MILLS	Completed	05/01/2011	05/01/2011
	Pred Name		Responsibility	Finish
	Design Building Addition		MILLS	05/01/2011
	Succ. Name		Responsibility	Start
	Assemble Brick Samples		NOLAN	05/01/2011
	Assemble Technical Data for Heat Pump		MILLS	05/01/2011
	Assemble and Submit Flooring Samples		HARIS	05/01/2011
	Begin Building Construction		FOLEY	05/01/2011
Assemble Brick Samples	NOLAN	Completed	05/01/2011	05/01/2011
	Pred Name		Responsibility	Finish
	Review and Approve Designs		MILLS	05/01/2011
	Succ. Name		Responsibility	Start
	Review and Approve Brick Samples		NOLAN	05/01/2011
Assemble Technical Data for Heat Pump	MILLS	Completed	05/01/2011	05/01/2011
	Pred Name		Responsibility	Finish
	Review and Approve Designs		MILLS	05/01/2011
	Succ. Name		Responsibility	Start
	Review Technical Data on Heat Pumps		MILLS	05/01/2011
Assemble and Submit	HARIS	Completed	05/01/2011	05/01/2011

Activity Resource Assignments

Activity (ID)	Duration	Start	Finish								
Design Building Addition (EC1000)	417.6	11/01/2010	01/19/2011								
<table> <tr> <th>Resource Name</th><th>Duration</th><th>Start</th><th>Finish</th></tr> <tr> <td>Paul Kim</td><td>441.6</td><td>11/01/2010</td><td>01/19/2011</td></tr> </table>				Resource Name	Duration	Start	Finish	Paul Kim	441.6	11/01/2010	01/19/2011
Resource Name	Duration	Start	Finish								
Paul Kim	441.6	11/01/2010	01/19/2011								
Start Office Building Addition Project (EC1010)	0	11/01/2010	11/01/2010								
Review and Approve Designs (EC1030)	172.8	01/17/2011	02/17/2011								
<table> <tr> <th>Resource Name</th><th>Duration</th><th>Start</th><th>Finish</th></tr> <tr> <td>Paul Kim</td><td>172.8</td><td>01/17/2011</td><td>02/17/2011</td></tr> </table>				Resource Name	Duration	Start	Finish	Paul Kim	172.8	01/17/2011	02/17/2011
Resource Name	Duration	Start	Finish								
Paul Kim	172.8	01/17/2011	02/17/2011								
Assemble Brick Samples (EC1040)	0	02/17/2011	02/17/2011								
Assemble Technical Data for Heat Pump (EC1050)	57.6	02/16/2011	02/25/2011								
<table> <tr> <th>Resource Name</th><th>Duration</th><th>Start</th><th>Finish</th></tr> <tr> <td>Paul Kim</td><td>57.6</td><td>02/16/2011</td><td>02/25/2011</td></tr> </table>				Resource Name	Duration	Start	Finish	Paul Kim	57.6	02/16/2011	02/25/2011
Resource Name	Duration	Start	Finish								
Paul Kim	57.6	02/16/2011	02/25/2011								
Assemble and Submit Flooring Samples (EC1060)	0	02/25/2011	02/25/2011								
Review and Approve Brick Samples (EC1070)	240	02/28/2011	04/13/2011								
<table> <tr> <th>Resource Name</th><th>Duration</th><th>Start</th><th>Finish</th></tr> <tr> <td>Paul Kim</td><td>240</td><td>02/28/2011</td><td>04/13/2011</td></tr> </table>				Resource Name	Duration	Start	Finish	Paul Kim	240	02/28/2011	04/13/2011
Resource Name	Duration	Start	Finish								
Paul Kim	240	02/28/2011	04/13/2011								
Review and Approve Flooring (EC1080)	224	02/25/2011	04/11/2011								
<table> <tr> <th>Resource Name</th><th>Duration</th><th>Start</th><th>Finish</th></tr> <tr> <td>Paul Kim</td><td>224</td><td>02/25/2011</td><td>04/11/2011</td></tr> </table>				Resource Name	Duration	Start	Finish	Paul Kim	224	02/25/2011	04/11/2011
Resource Name	Duration	Start	Finish								
Paul Kim	224	02/25/2011	04/11/2011								
Begin Building Construction (EC1090)	0	02/28/2011	02/28/2011								
Site Preparation (EC1100)	345.6	02/23/2011	04/18/2011								
<table> <tr> <th>Resource Name</th><th>Duration</th><th>Start</th><th>Finish</th></tr> <tr> <td>Excavator</td><td>345.6</td><td>02/23/2011</td><td>04/18/2011</td></tr> </table>				Resource Name	Duration	Start	Finish	Excavator	345.6	02/23/2011	04/18/2011
Resource Name	Duration	Start	Finish								
Excavator	345.6	02/23/2011	04/18/2011								
Review Technical Data on Heat Pumps (EC1160)	216	02/24/2011	04/06/2011								
<table> <tr> <th>Resource Name</th><th>Duration</th><th>Start</th><th>Finish</th></tr> <tr> <td>Paul Kim</td><td>216</td><td>02/24/2011</td><td>04/06/2011</td></tr> </table>				Resource Name	Duration	Start	Finish	Paul Kim	216	02/24/2011	04/06/2011
Resource Name	Duration	Start	Finish								
Paul Kim	216	02/24/2011	04/06/2011								
Prepare and Solicit Bids for Flooring (EC1170)	192	04/04/2011	05/06/2011								

Schedule Report with Notebooks

Activity	Activity Status	BL1 Start	Start	BL1 Finish	Finish
Review Bids for Heat Pump(EC1240)	Not Started	04/20/2011	05/03/2011	05/03/2011	05/17/2011
Review Bids for Flooring(EC1250)	Not Started	04/22/2011	05/06/2011	05/13/2011	05/27/2011
Award Contract for Brick(EC1260)	In Progress	04/29/2011	04/21/2011A	05/06/2011	05/05/2011
Award Contract for Heat Pump(EC1270)	Not Started	05/04/2011	05/17/2011	05/11/2011	05/25/2011
Deliver Brick(EC1280)	Not Started	05/06/2011	05/05/2011	05/09/2011	05/06/2011
Fabricate and Deliver Heat Pump and Controls(EC1290)	Not Started	05/12/2011	05/25/2011	12/24/2012	01/04/2013
Award Contract for Flooring(EC1300)	Not Started	05/13/2011	05/27/2011	05/19/2011	06/03/2011
Fabricate and Deliver Flooring(EC1310)	Not Started	05/20/2011	06/03/2011	06/13/2012	06/27/2012
Install Underground Water Lines(EC1320)	Not Started	05/20/2011	06/03/2011	06/06/2011	06/20/2011
Notebook Topics: Anticipated Problems Notebook Description: Grading and soil conditions will slow this operation. Check estimate. Also, Plumber availability is limited for this work.					
Install Underground Electric Conduit(EC1330)	Not Started	05/20/2011	06/03/2011	06/06/2011	06/20/2011
Form/Pour Concrete Footings(EC1340)	Not Started	06/07/2011	06/21/2011	07/08/2011	07/22/2011
Concrete Foundation Walls(EC1350)	Not Started	07/11/2011	07/25/2011	08/11/2011	08/25/2011

Resource Role Skill Sets

Resource (Role count)

	Role	Primary Role	Proficiency
Painter (1)			
	Trades	Yes	3 - Skilled
Project Managers (1)			
	Management	Yes	3 - Skilled
Paul Kim (1)			
	Management	Yes	3 - Skilled
Dan Sharpe (1)			
	Developer	Yes	3 - Skilled
Alice Wynn (2)			
	Lean Six Sigma Specialist	No	3 - Skilled
	Product Tester	Yes	3 - Skilled
Rea Johnson (1)			
	Project Leader	Yes	3 - Skilled
Deepak Singh (2)			
	DBA	No	3 - Skilled
	Quality Assurance	Yes	3 - Skilled
Gary Marshall (3)			
	Product Tester	No	3 - Skilled
	Product Analyst	Yes	3 - Skilled
	Product Designer	No	3 - Skilled
Larry West (2)			
	Product Manager	Yes	3 - Skilled
	Product Project Manager	No	3 - Skilled
Sue Baxter (2)			

Resource Code Assignments

Resource Code		
	Code Value	Resource Name
Classification	CONTR	Gary Marshall
		Conveying Subcontractor
		Roofing Subcontractor
		Utilities Subcontractor
		BPM Consultant 1
		Millwork Subcontractor
		Thermal Protection Subcontractor
		Finishes & Fit-out Subcontractor
		Fire Suppression Subcontractor
		IT Consultant
		Sue Baxter
		Specialty Metal Fabricator Subcontractor
		FF&E Specialties
		BPM Consultant 2
		Drywall Subcontractor
		BPM Consultant 3
		Paul Riley
		Glass & Glazing Subcontractor
		Paving & Roadways Subcontractor
		Pool Installation Subcontractor
		Landscaping Subcontractor
		Concrete Foundation Subcontractor
	PTIC	Molly Abraham
		Alice Wynn
		Lori McNeil
	FTTrade	Operator

Resource Role Associations

Role (count)

Resource (ID)	Proficiency	Primary Role
Process Architect (5)		
Judy Billings (BillingsJ)	3 - Skilled	Yes
Frank Chu (Chuf)	2 - Expert	Yes
Wayne Prescott (PrescottW)	3 - Skilled	Yes
Michelle Peterson (PetersonM)	4 - Proficient	No
Ben Frost (FrostB)	2 - Expert	No
Accounting (2)		
Project Controls (Project Controls)	3 - Skilled	No
Administrator (Admin)	3 - Skilled	No
Business Analyst (4)		
Ian Vincent (VincentI)	3 - Skilled	No
Jo Wren (WrenJ)	3 - Skilled	No
IT Consultant (ITCon)	3 - Skilled	Yes
Carina Bennett (BennettC)	3 - Skilled	No
Business Analyst Level 1 (1)		
Michelle Peterson (PetersonM)	3 - Skilled	Yes
Change Management Coordinator (1)		
Peter Cooper (CooperP)	3 - Skilled	Yes
Consultant (4)		
External Contractors (Contr)	3 - Skilled	Yes
BPM Consultant 3 (Bpm003)	3 - Skilled	Yes
BPM Consultant 2 (Bpm002)	3 - Skilled	Yes
BPM Consultant 1 (Bpm001)	3 - Skilled	Yes
Civil/Structural Crews (0)		
DBA (2)		

Code Assignments

<u>Location</u>

Europe

Europe

Katalyst Virtualization

<u>Location</u>

Russia

Russia

Project Swordfish

<u>Location</u>

Europe

Europe

Zenith Continuity Program

<u>Location</u>

Latin America

Latin America

ACH Integration Project

<u>Location</u>

India

India

ERP Legacy Merge

<u>Location</u>

Latin America

Latin America

Project Portfolio Review

Project(ID)	Project Manager	Project Location	Current Phase	Planned Start	Data Date
-------------	-----------------	------------------	---------------	---------------	-----------

Haitang Corporate Park(EC00501)	Chen	China	Development	09/01/2010	05/01/2011
ISSUE		PRIORITY		STATUS	
qsdfsaf		Normal		Closed	
City Center Office Building Addition(EC00515)	Thomas	Europe	Design	11/01/2010	05/01/2011
Nesbid Building Expansion(EC00530)	Pell	India	Initiation	07/01/2011	07/01/2011
Harbour Pointe Assisted Living Center(EC00610)	Jones	Australia	Development	09/01/2010	05/01/2011
ISSUE		PRIORITY		STATUS	
Building 2 Subject To Delay		High		Closed	
Finish Date Variance (days) is -21d on WBS: Harbour Pointe.2.4		Normal		Closed	
Finish Date Variance (days) is -6d on WBS: Harbour Pointe.1.2		Normal		Closed	
Forecast Overrun		Top		Closed	
Unit Finishes Experiencing Productivity Delays		High		Closed	
RISK		STATUS		TYPE	
Concrete supply constrained		Closed		Threat	
Site access restricted for 2 weeks		Closed		Threat	
Weather delay due to hurricane		Closed		Threat	
Poor ground conditions		Closed		Threat	
Failed electrical inspection		Closed		Threat	

Project Portfolio Review

Project(ID)	Project Manager	Project Location	Current Phase	Planned Start	Data Date
-------------	-----------------	------------------	---------------	---------------	-----------

Interior design changes
 Contractor financial instability
 Permit delay
 Window manufacturing delay
 Weather delay due to unusually wet weather
 New roof coating cuts roof install time

Closed Threat
 Closed Threat
 Closed Threat
 Closed Threat
 Closed Threat
 Closed Opportunity

NOTEBOOK TOPIC

NOTEBOOK DESCRIPTION

Recent Accomplishments

Recently past structural and traffic inspection. No weather delays in the past month allowed us to pull in finish date by a week. We successfully accomplished some work that had risk identified. The risks did not occur and we can now release 100k in contingency funds.

Sponsor Feedback

Owner is happy with progress and completed a walk through during the month. They do anticipate a few changes, primarily around the curbing and the reception area.

Juniper Nursing Home(EC00620)	Cortez	Latin America	Design	11/01/2010	05/01/2011
-------------------------------	--------	---------------	--------	------------	------------

ISSUE

PRIORITY

STATUS

Building 2 Subject To Delay
 Finish Date Variance (days) is -21d on WBS: Harbour
 Pointe.2.3
 Finish Date Variance (days) is -21d on WBS: Harbour
 Pointe.2.4

High Closed
 Normal Closed
 Normal Closed

Project Portfolio Review


Project(ID)	Project Manager	Project Location	Current Phase	Planned Start	Data Date
Finish Date Variance (days) is -21d on WBS: Harbour Pointe.2.5		Normal	Closed		
Finish Date Variance (days) is -26d on WBS: Harbour Pointe.8		Normal	Closed		
Finish Date Variance (days) is -36d on WBS: Harbour Pointe.5		Normal	Closed		
Finish Date Variance (days) is -6d on WBS: Harbour Pointe.1.2		Normal	Closed		
Forecast Overrun		High	Closed		
Unit Finishes Experiencing Productivity Delays		High	Closed		
Saratoga Senior Community(EC00630)	Jones	North America	Initiation	06/01/2011	06/01/2011
ISSUE		PRIORITY	STATUS		
Building 2 Subject To Delay		High	Closed		
Finish Date Variance (days) is -21d on WBS: Harbour Pointe.2.3		Normal	Closed		
Finish Date Variance (days) is -21d on WBS: Harbour Pointe.2.4		Normal	Closed		
Finish Date Variance (days) is -21d on WBS: Harbour Pointe.2.5		Normal	Closed		
Finish Date Variance (days) is -26d on WBS: Harbour Pointe.8		Normal	Closed		
Finish Date Variance (days) is -36d on WBS: Harbour Pointe.5		Normal	Closed		
Finish Date Variance (days) is -6d on WBS: Harbour Pointe.1.2		Normal	Closed		
Forecast Overrun		High	Closed		
Unit Finishes Experiencing Productivity Delays		High	Closed		

Portfolio Counts

Project Count: 6
Activity Count: 608

Issues


Open: 24

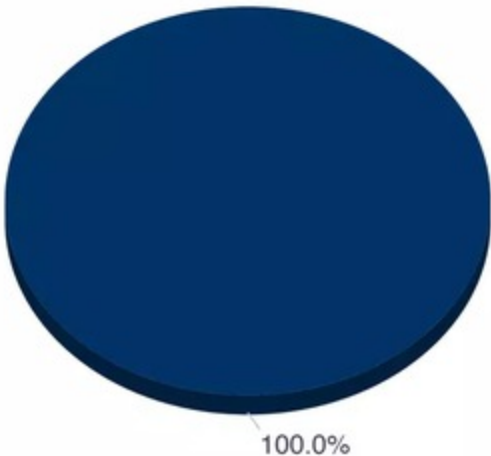

■ Open

Risks

Opportunity:1
Threat:10

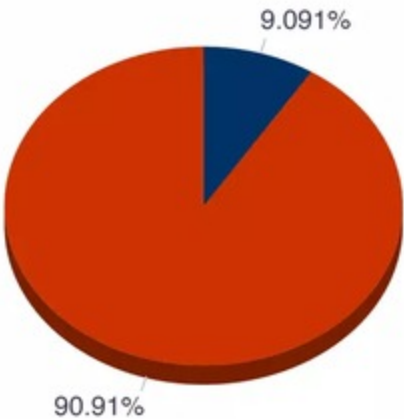

■ Opportunity
■ Threat

Document Assignments

Document Category

Activity Name

Detailed Design Specifications

Assemble Technical Data for Heat Pump

Document Title	Deliverable	Work Product	WBS Name
Detailed Design Specification	N	N	Design and Engineering

Design Building Addition

Document Title	Deliverable	Work Product	WBS Name
Detailed Design Specification	N	N	Design and Engineering

Assemble Technical Data for Heat Pump

Document Title	Deliverable	Work Product	WBS Name
Design	N	N	Design and Engineering

Design Building Addition

Document Title	Deliverable	Work Product	WBS Name
Design	N	N	Design and Engineering

Project Summary

Project ID: EC00515	Data Date: 05/01/2011
Project Name: City Center Office Building Addition	Finish: 07/03/2013
Total Activities: 71	At Completion Cost: \$745,786
Completed: 13	Actual Cost to Date: \$124,028
In Progress: 3	Remaining Total Cost: \$621,758

Risk Summary

Report Date:	Open Risks:
Total Risks:	Active Risks:
Threats:	Rejected (Closed):
Opportunities:	Managed (Closed):
Proposed Risks:	Impacted (Closed):

Risk by Tolerance Threshold

Probability

Impacts

Schedule
Cost

Tolerance

Probability and Impact Scoring (PID)

Risk Score is based on: **Highest Impact**

Impact

Severity 1	Severity 2	Severity 3
------------	------------	------------

Key



As of: 05/01/2011

Project Status Report for: **City Center Office Building Addition (EC00515)**

SPONSOR Forsyth		BUSINESS SEGMENT 1004050		PROJECT MANAGER Thomas		CURRENT PHASE Design		LOCATION Europe			
DESCRIPTION Project is for the addition to the office building in center city. This includes design and construct work.											
START 11/01/2010		FINISH 07/03/2013		TARGET FINISH 06/19/2013		% COMPLETE 14.88%		ACTIVITIES COMPLETED 13 of 71		PROJECT SCORE 80	
APPROVED BUDGET \$734,195		COST TO DATE \$124,028		AT COMPLETION \$745,786		COST VARIANCE -\$11,591		LABOR TO DATE 2038 h		LABOR VARIANCE -201.4 h	

PRIORITY ISSUES

0 priority of 0 issues

OPEN RISKS

0 open of 0 risks

NOTEBOOKS

MILESTONES

	Date	Status
Assemble Brick Samples	2/15/2011	Completed
Assemble and Submit Flooring Samples	2/15/2011	Completed
Begin Building Construction	2/15/2011	Completed
Begin Structural Phase	11/10/2011	Not Started
Building Addition Complete	6/19/2013	Not Started



Project Summary

Project ID	EC00515	Data Date	
Project Name	City Center Office Building Addition	Finish	
Total Activities	71	At Completion Cost	
Completed	13	Actual Cost to Date	\$124,028
In Progress	3	Remaining Total Cost	

Risk Summary

Risks by Tolerance Threshold

Project Hierarchy Including Steps

WBS Code	WBS Code Name			
	Activity Name(ID)	Status	Start	Finish
Interior Finishes	Interior Finishes			
	Drywall in Offices (EC1700)	Not Started	02/05/2013	03/27/2013
	Touch-up and Clean-up (EC1820)	Not Started	06/19/2013	06/21/2013
	Finishes Complete (EC1840)	Not Started	06/26/2013	06/26/2013
	Punch List (EC1850)	Not Started	06/26/2013	07/03/2013
	Building Addition Complete (EC1860)	Not Started	07/03/2013	07/03/2013
	Exterior Finishes			
	Close-In Phase Begins (EC1590)	Not Started	05/15/2012	05/15/2012
	Building Enclosed (EC1620)	Not Started	06/18/2012	06/18/2012
	Foundation			
	Begin Building Construction (EC1090)	Completed	02/28/2011A	02/28/2011A
	Site Preparation (EC1100)	Completed	02/23/2011A	04/18/2011A
	Excavation (EC1230)	Not Started	05/02/2011	06/02/2011
	Install Underground Water Lines (EC1320)	Not Started	06/03/2011	06/20/2011
	Install Underground Electric Conduit (EC1330)	Not Started	06/03/2011	06/20/2011
	Form/Pour Concrete Footings (EC1340)	Not Started	06/21/2011	07/22/2011
	Concrete Foundation Walls (EC1350)	Not Started	07/25/2011	08/25/2011
	Form and Pour Slab (EC1360)	Not Started	08/26/2011	09/12/2011
	Backfill and Compact Walls (EC1370)	Not Started	09/13/2011	09/19/2011
	Foundation Phase Complete (EC1380)	Not Started	09/19/2011	09/19/2011
	Structure			
	Erect Structural Frame (EC1390)	Not Started	09/19/2011	11/24/2011
	Begin Structural Phase (EC1410)	Not Started	11/24/2011	11/24/2011
	Floor Decking (EC1420)	Not Started	11/24/2011	01/11/2012
	Concrete First Floor (EC1430)	Not Started	01/11/2012	03/01/2012
	Erect Stairwell and Elevator Walls (EC1460)	Not Started	03/01/2012	04/04/2012
	Concrete Basement Slab (EC1470)	Not Started	03/01/2012	04/04/2012

Users

Login Name	Personal Name	Resource	Global Profile
admin	admin	MathisL	<Admin Superuser>
biadmin	biadmin	Trades	<Admin Superuser>
user01	user01	Product Dev	<Admin Superuser>
user02	user02		<Admin Superuser>

Project Template Management

Template Name	Division	Added By	Date Added
Business Process Template		admin	8/12/2010
Assisted Living Facility		admin1	9/7/2010
IT Template		admin	8/12/2010
Product Development Template		admin	8/12/2010

Profile Privileges

Profile Scope

Security Profile

Security Privilege

GLOBAL

<No Global Privileges>

Administrator

Add Global Activity Codes

Add Global Issue Codes

Add Project Codes

Add Resource Codes

Add Resources

Add/Delete Secure Codes

Add/Edit/Delete Activity Step Templates

Add/Edit/Delete Categories and Overhead Codes

Add/Edit/Delete Cost Accounts

Add/Edit/Delete Currencies

Add/Edit/Delete Financial Period Dates

Add/Edit/Delete Funding Sources

Add/Edit/Delete Global Activity and Assignment Layouts, Views and Filters

Add/Edit/Delete Global Calendars

Add/Edit/Delete Global Dashboards

Add/Edit/Delete Global Portfolios

Add/Edit/Delete Global Project, WBS and Portfolio Layouts, Views and Filters

Add/Edit/Delete Global Reports

Add/Edit/Delete Global Resource and Role Teams

Add/Edit/Delete Global Scenarios

Add/Edit/Delete Issue Forms

Add/Edit/Delete Microsoft Project Templates

Add/Edit/Delete OBS

Add/Edit/Delete Project Templates

Add/Edit/Delete Rate Types and Units of Measure

Add/Edit/Delete Resource Calendars

Profile Privileges

Profile Scope

Security Profile

Security Privilege

Add/Edit/Delete Resource Curves
Add/Edit/Delete Risk Categories, Matrices, and Thresholds
Add/Edit/Delete Roles
Add/Edit/Delete Security Profiles
Add/Edit/Delete Timesheet Period Dates
Add/Edit/Delete User Defined Fields
Add/Edit/Delete User Interface Views
Add/Edit/Delete Users
Administer Global External Applications
Administer Scheduled Services
Approve Resource Timesheets
Assign Secure Codes
Delete Global Activity Codes
Delete Global Issue Codes
Delete Project Codes
Delete Resource Codes
Delete Resources
Edit Application Settings
Edit Global Activity Codes
Edit Global Change Definitions
Edit Global Issue Codes
Edit Global Tracking Layouts
Edit Project Codes
Edit Projects from Scorecards
Edit Resource Codes
Edit Resources
Edit Secure Codes
Import Project Management XER, MPP, MPX, and P3
Import XLS
Import XML

Profile Privileges

Profile Scope

Security Profile

Security Privilege

Provision Users from LDAP

View All Global/Project Data via SDK

View Resource Role Proficiency

View Resource and Role Costs/Financials

View Secure Codes

Executive / Stakeholder

Add Project Codes

Add Resource Codes

Add/Delete Secure Codes

Add/Edit/Delete Funding Sources

Add/Edit/Delete Global Activity and Assignment Layouts, Views and Filters

Add/Edit/Delete Global Portfolios

Add/Edit/Delete Global Project, WBS and Portfolio Layouts, Views and Filters

Add/Edit/Delete Global Resource and Role Teams

Add/Edit/Delete Resource Curves

Add/Edit/Delete Security Profiles

Add/Edit/Delete User Defined Fields

Add/Edit/Delete Users

Approve Resource Timesheets

Assign Secure Codes

Delete Project Codes

Delete Resource Codes

Edit Global Tracking Layouts

Edit Project Codes

Edit Projects from Scorecards

Edit Resource Codes

Edit Secure Codes

Calendar Use

Calendar Name

Corporate - Standard Full Time (Default Calendar)

Project ID	Project Name	Resource ID	Resource Name
CORP00591	Order Management Redesign	AndersonG	Glen Anderson, VP Development
CORP00424	Lead Qualification Project	VincentI	Ian Vincent
CORP00307	Online Invoice Generation Project	CharlesM	Mandy Charles, VP IT Ops
CORP00103	Order Fullfillment Phase II	ZhuS	Shannon Zhu
CORP00768	Logistics Reengineering Program	LaffertyV	Vanessa Lafferty
CORP00118	GIS Interface Project	BennettC	Carina Bennett
CORP00712	Cash Flow BI Project	PaxsonD	Dan Paxson
CORP00595	Nexus Project	SinghD	Deepak Singh
CORP00852	eBusiness Transformation Program	SharpeD	Dan Sharpe
CORP00384	Alliance Portal Integration Project	ITCon	IT Consultant
PROD00914	Project Nano	LiR	Roy Li
PROD00414	4G Tablet Project	RiceB	Barbara Rice, PMO Director
PROD00111	Magna Pad Product Test	ChopraA	Amit Chopra
PROD00228	Xstar Release II	AbrahamM	Molly Abraham
